



Republic of the Philippines
Department of Health
'AMANG' RODRIGUEZ MEMORIAL MEDICAL CENTER
Marikina City
"Philhealth-Accredited"



**Design and Build Services for the Phase I of Construction of Eight (8) Storey
Multi-Specialty Center Building**

Name of Contractor: **E.M. CUERPO, INC.**

Location of the Project: **Sumulong Highway, Sto. Niño, Marikina City**

Project cost: **Php 130,833,333.66**

Start of construction: **October 30, 2018**

Target date of completion: **August 12, 2021 (revised target; with time extensions and time suspension due to COVID-19 pandemic)**

Description of the project: **This project covers the design of an eight (8) storey multispecialty center building and construction of the structural framework from basement to 3rd Floor including functional portion of 2nd Floor of the structure (from the original construction of the entire structural framework-Variation Order No.3).**

Source of Fund: **HFEP**

Implementing Office: **'Amang' Rodriguez Memorial Medical Center**

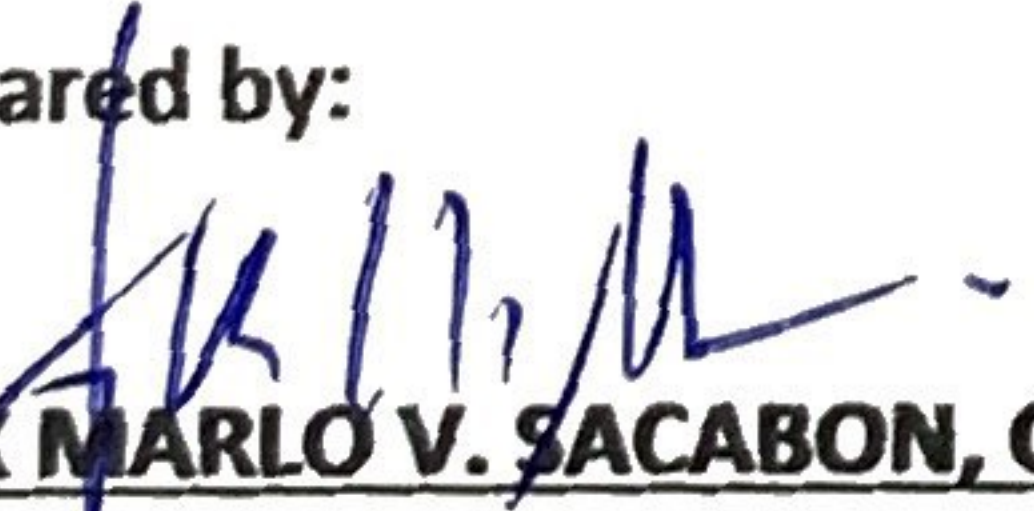
Responsible official: **Imelda M. Mateo, MD, MBAH, FPCP, FPCCP**

Contact number and email address: **amangrod@yahoo.com / 8941-5854 local 111**


Completion rate: **61.74 % (as of March 31, 2021 – 1st Quarter of 2021)**


Project status: **On-going**

Prepared by:


ALEX MARLO V. SACABON, CE, MMPA
Training Specialist IV


DENNIS L. BARRAMEDA, ME, RMP
Engineer III


JOSEKITO F. ENRIQUEZ, ME
Engineer III


ARNOLD NICOLE G. CAÑA, JR., CE
Engineer II

Noted by:


DANILO S. SUMALANGCAY, REE
Engineer IV

Recommending Approval:


ENRICO P. RAGAZA, MD, FPCS, FPSCRS, FPSGS
Acting Chief of Medical Professional Staff II

Approved by:


IMELDA M. MATEO, MD, MBAH, FPCP, FPCCP
Medical Center Chief II




Republic of the Philippines
Department of Health
'AMANG' RODRIGUEZ MEMORIAL MEDICAL CENTER
Marikina City
"Philhealth-Accredited"




**Expansion of the Out-Patient Department (OPD) Building including repair/renovation of affected areas,
Phase II (Construction of 2 additional floors of OPD)**

Name of Contractor: **TOKWING CONSTRUCTION CORPORATION**
Location of the Project: **Sumulong Highway, Sto. Niño, Marikina City**
Project cost: **Php 39,600,794.18**
Start of construction: **October 23, 2019**
Target date of completion: **June 27, 2021 (revised target; with time extensions and time suspension due to COVID-19 pandemic)**
Description of the project: **This project covers the construction of two additional floors of the OPD Building and repair/ renovation of affected areas.**
Source of Fund: **HFEP**
Implementing Office: **'Amang' Rodriguez Memorial Medical Center**
Responsible official: **Imelda M. Mateo, MD, MBAH, FPCP, FPCCP**
Contact number and email address: **amangrod@yahoo.com / 8941-5854 local 111**
Completion rate: **66.60% (as of March 31, 2021 - 1st Quarter of 2021)**
Project status: **On-going**

Prepared by:


ALEX MARLO V. SACABON, CE, MMPA
Training Specialist IV


DENNIS L. BARRAMEDA, ME, RMP
Engineer III



JOSELITO F. ENRIQUEZ, ME
Engineer III


ARNOLD NICOLE G. CAÑA, JR., CE
Engineer II

Noted by:


DANILO S. SUMALANGCAY, REE
Engineer IV

Recommending Approval:


ENRICO P. RAGAZA, MD, FPCS, FPSCRS, FPSGS
Acting Chief of Medical Professional Staff II

Approved by:


IMELDA M. MATEO, MD, MBAH, FPCP, FPCCP
Medical Center Chief II
